

LAB 2 REPORT

Agile Backlog Creation & Sprint Simulation in Jira

Project: Smart Parking Space Rental & License Validator

Student Name	Prakash Heroor
Project	Smart Parking Space Rental & License Validator
Domain	Smart Cities, Transport & Logistics
Users	Vehicle Owner, Parking Warden

❖ Objective

To convert functional requirements into Agile backlog items, organize them into an Epic and User Stories, prioritize and estimate the stories, simulate a Scrum sprint in Jira, and analyze sprint progress using the Burndown Chart.

❖ 2. Epic

Epic Name	Smart Parking Space Management
Description	Enable vehicle owners to easily find, rent, and manage available parking spaces through a smart parking system. The system should allow users to view parking availability, select suitable parking spaces, and manage their parking rentals efficiently.

❖ 3. User Stories, Priority & Story Points

The following five User Stories were created under the Epic. The stories follow the required Agile format: As a [user role], I want [goal], so that [benefit].


Issue	Story	User	User Story	Priority	Points
SPSRLV-2	View Available Parking Spaces	Vehicle Owner	As a vehicle owner, I want to view available parking spaces, so that I can find a suitable parking spot.	High	3

SPSRLV-3	Search Parking Space	Vehicle Owner	As a vehicle owner, I want to search for parking spaces based on location and availability, so that I can quickly find convenient parking.	High	5
SPSRLV-4	Rent Parking Space	Vehicle Owner	As a vehicle owner, I want to rent an available parking space, so that I can reserve a parking spot for my vehicle.	High	8
SPSRLV-5	Validate Vehicle License	Parking Warden	As a parking warden, I want to validate a vehicle's license, so that I can ensure that only authorized vehicles use the parking facility.	Medium	5
SPSRLV-6	Manage Parking Rentals	Vehicle Owner	As a vehicle owner, I want to view and manage my parking rentals, so that I can keep track of my reserved parking spaces.	Medium	3

Total Story Points: 24


❖ 4. Jira Backlog

The Jira backlog contains the five User Stories under the Smart Parking Space Management Epic. The backlog also displays the assigned story points.

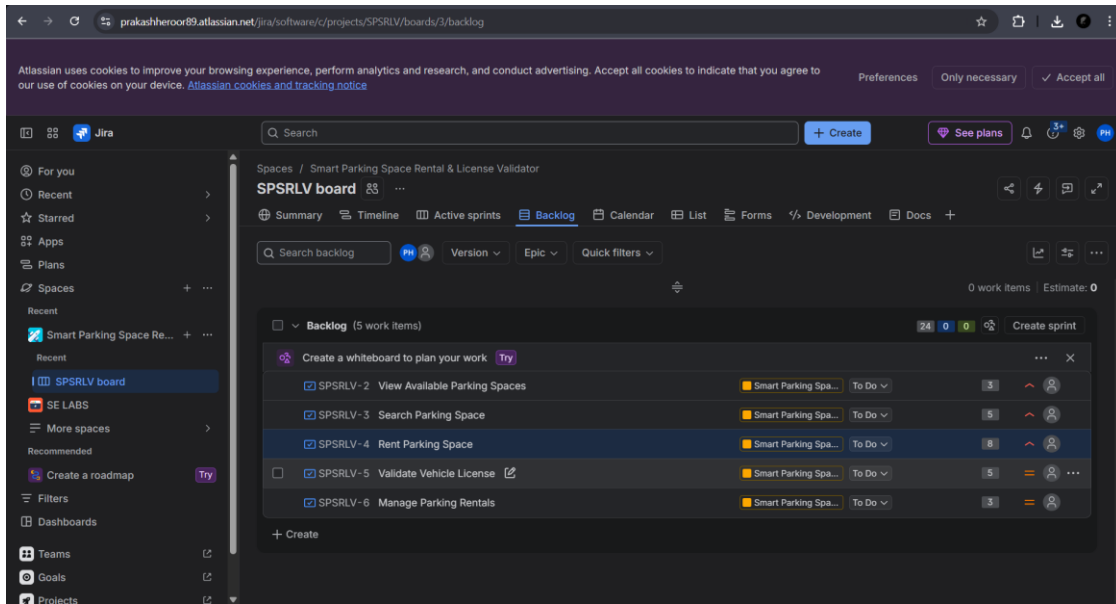


❖ 5. Sprint 1 Simulation

Sprint 1 was created and the five User Stories were selected for the sprint. The sprint was started as a one-week sprint. During the simulation, the stories were moved through the Scrum workflow from To Do to In Progress and then to Done.

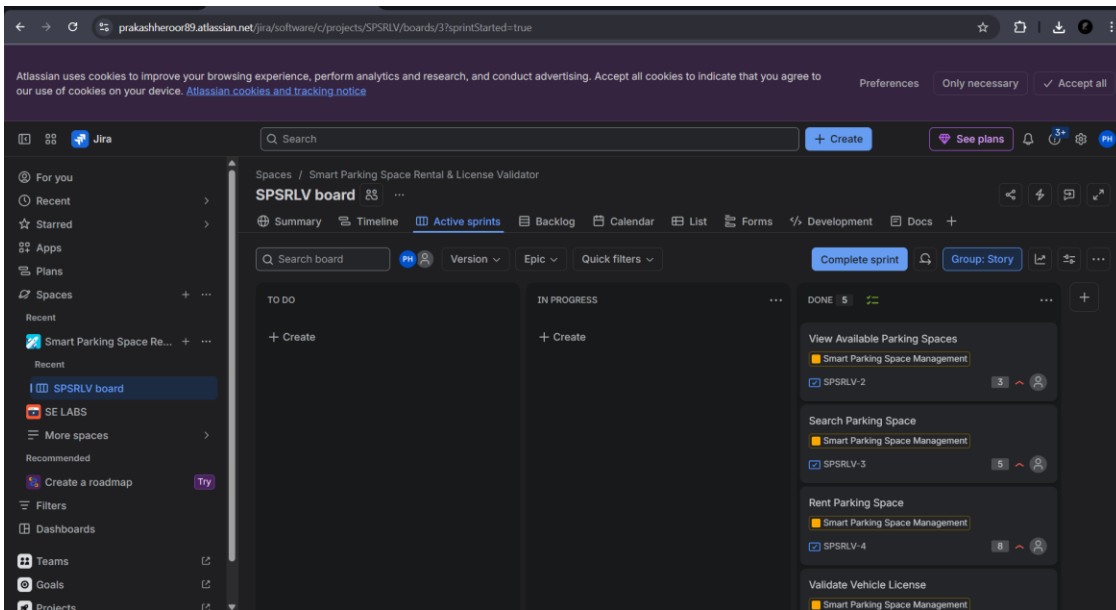

❖ 6. Burndown Chart

The Burndown Chart tracks the amount of remaining work during Sprint 1. The chart uses Story Points as the estimation statistic. The sprint started with 24 story points, and the guideline shows the expected linear reduction of work over time.

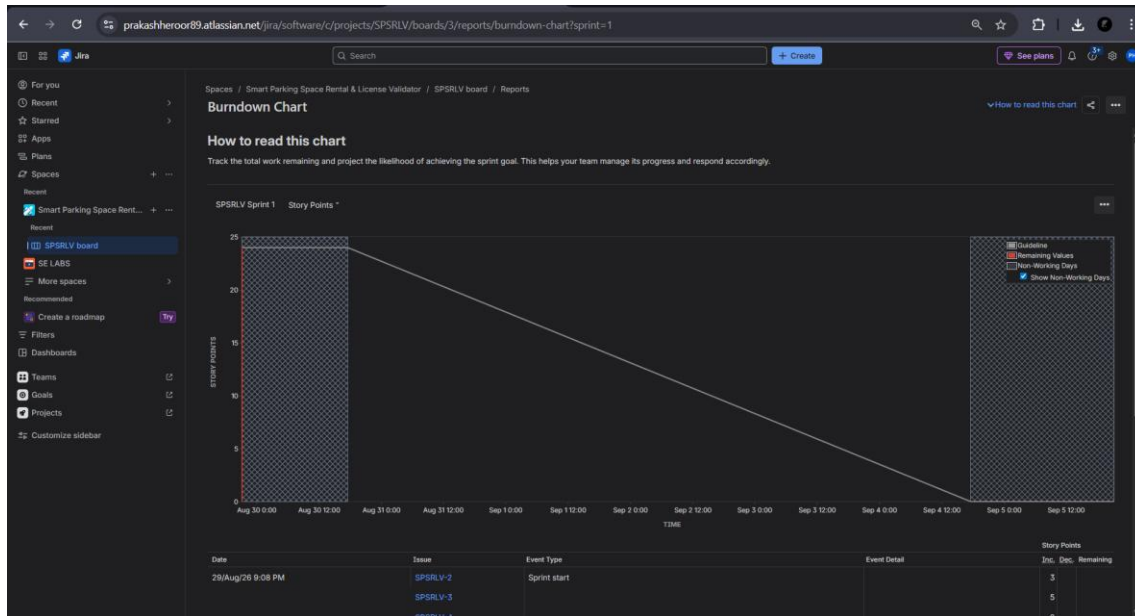

❖ 7. Reflection Questions

1. Did your estimations reflect the actual effort?

The estimations provided a reasonable relative measure of effort for the simulated sprint. The larger story, Rent Parking Space, was assigned 8 points because it involves more complexity than the other stories. Since this was a simulated sprint, the story points mainly represent relative complexity and uncertainty rather than exact development time.

2. Was your backlog well-prioritized?

Yes. The core parking functions were given High priority because they directly support the main objective of the system. View Available Parking Spaces, Search Parking Space, and Rent Parking Space were prioritized first. License validation and rental management were given Medium priority.

3. How did your simulated sprint align with your plan?

The sprint followed the planned Scrum workflow. The selected stories were added to Sprint 1 and progressed through the board. The simulation demonstrated the movement of work from To Do to In Progress and finally to Done.

4. What insights did the burndown chart give about your team's capacity?

The Burndown Chart showed the planned reduction of the 24 story points across the sprint. It provides a visual indication of remaining work and helps compare actual progress with the expected guideline. In this simulation, it also demonstrates how Jira can be used to monitor sprint progress and assess whether the team is on track.
